BIN BROOK FLOOD ALLEVIATION SCHEME APPROVAL TO CONSTRUCTION

ID	Task Name	Duration	Start	Finish
1	**PAR Submission and Approval**	**67 days**	**Thu 31/05/07**	**Fri 31/08/07**
2	Submit Final PAR to NRG	0 days	Thu 31/05/07	Thu 31/05/07
3	Meeting Date	0 days	Wed 27/06/07	Wed 27/06/07
4	PAR Approval	6 wks	Wed 27/06/07	Tue 07/08/07
5	Consultant prepare target for next stage	18 days	Wed 08/08/07	Fri 31/08/07
6	Award to consultant	0 days	Fri 31/08/07	Fri 31/08/07
7				
8	**Planning Approval Process**	**100 days**	**Mon 03/09/07**	**Fri 18/01/08**
9	Prepare Environmental Statement	6 wks	Mon 03/09/07	Fri 12/10/07
10	Consultation Period	6 wks	Mon 15/10/07	Fri 23/11/07
11	Finalise Environmental Statement	2 wks	Mon 26/11/07	Fri 07/12/07
12	Prepare Planning Application	4 wks	Mon 12/11/07	Fri 07/12/07
13	Prepare Mineral Extraction Licence	4 wks	Mon 12/11/07	Fri 07/12/07
14	Submit applications	0 days	Fri 07/12/07	Fri 07/12/07
15	Approvals received	0 days	Fri 18/01/08	Fri 18/01/08
16				
17	**Agreements with Cambridge Preservation Society**	**85 days**	**Wed 08/08/07**	**Tue 04/12/07**
18	Landscape design	6 wks	Mon 03/09/07	Fri 12/10/07
19	Land and compensation agreement	17 wks	Wed 08/08/07	Tue 04/12/07
20				
21	**Detailed Design and Tender Stage**	**150 days**	**Tue 01/04/08**	**Mon 27/10/08**
22	Prepare detailed design	20 wks	Tue 01/04/08	Mon 18/08/08
23	Prepare contract documentation	6 wks	Tue 08/07/08	Mon 18/08/08
24	Issue works information	0 days	Mon 18/08/08	Mon 18/08/08
25	Target setting	10 wks	Tue 19/08/08	Mon 27/10/08
26	Contract award	0 days	Mon 27/10/08	Mon 27/10/08
27				
28	**Construction Stage**	**440 days**	**Fri 18/01/08**	**Fri 25/09/09**
29	Instruct Cambridge Water to divert Main	0 days	Fri 18/01/08	Fri 18/01/08
30	Cambridge Water lead in period	6 mons	Mon 21/01/08	Fri 04/07/08
31	Cambridge Water divert main	12 wks	Mon 07/07/08	Fri 26/09/08
32	Construct flood storage area	25 wks	Mon 06/04/09	Fri 25/09/09

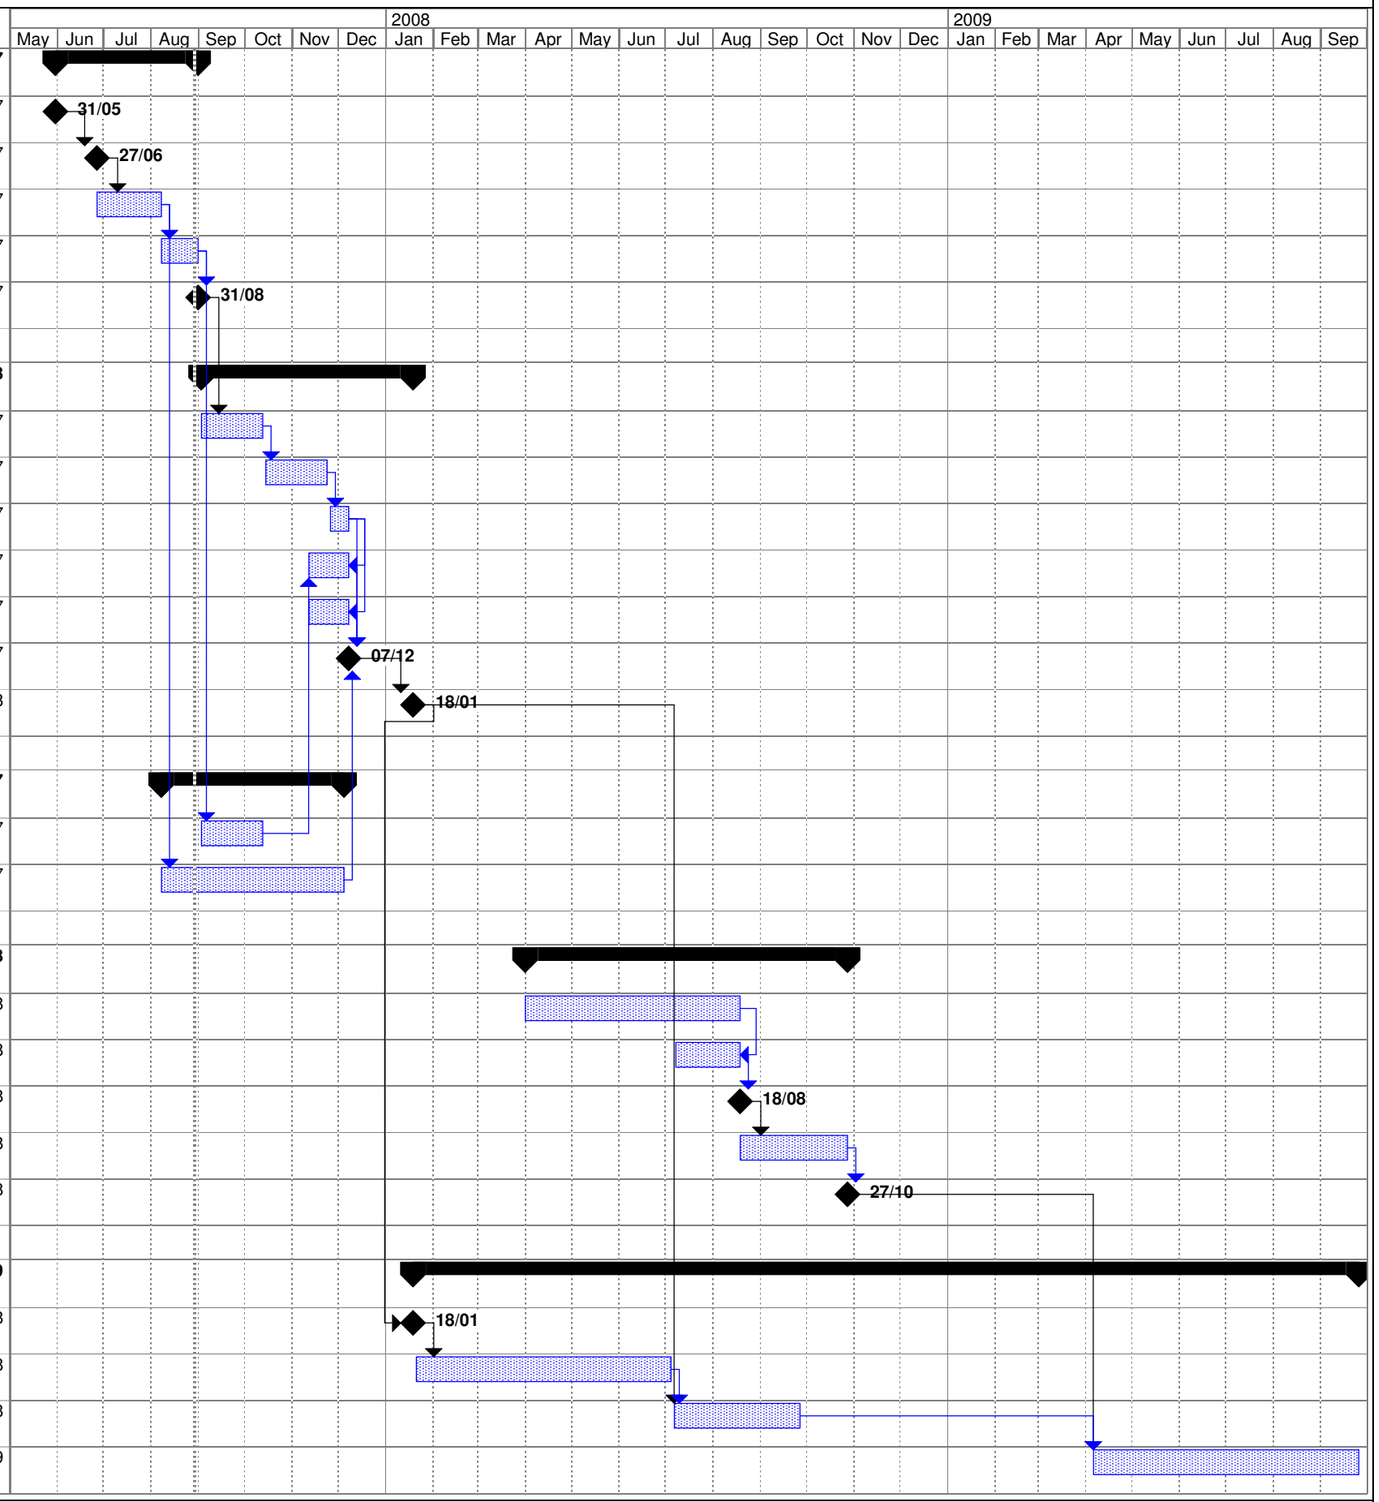

Bin Brook Flood Alleviation Scheme
Project Approval to Completion
Programme v1 15th February 2007

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
